

# Prop AA Projects Schedule

April 18, 2025

# CURRENT PROJECTS


## Canyon Crest Academy – Black Box Modernization

**Start Date: 3/4/25**

**Estimated Substantial Completion Date: August 2025**

**Funding Source: Prop AA**

**Status: MEP rough-in, footings and slab**

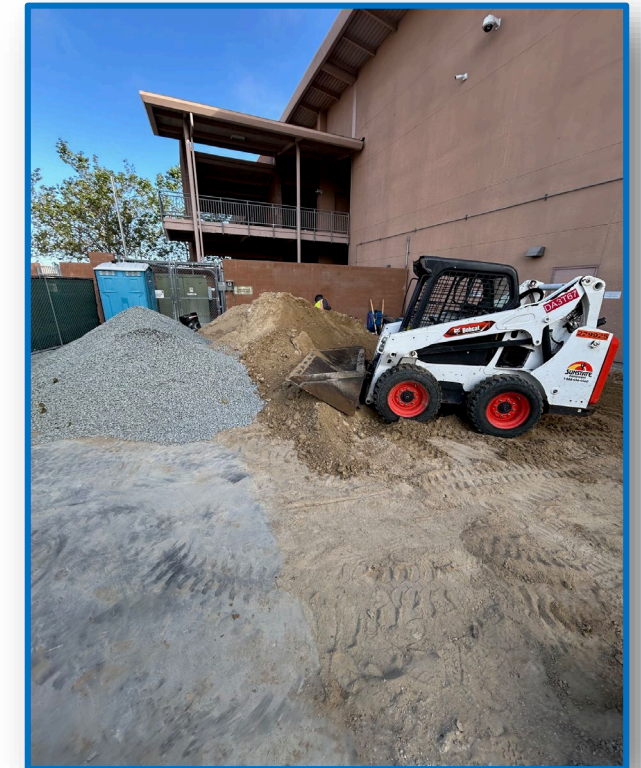

Photos as of 4/18/25



# CURRENT PROJECTS


## Diegueno Middle School – Bldgs. D, F & K Modernization Phase 2 and AV Technology Improvements

**Start Date: 4/22/24**

**Estimated Substantial Completion Date: 5/22/25**

**Funding Source: Prop AA, Fund 40 & Mello-Roos**

**Status: DSA Punch list**

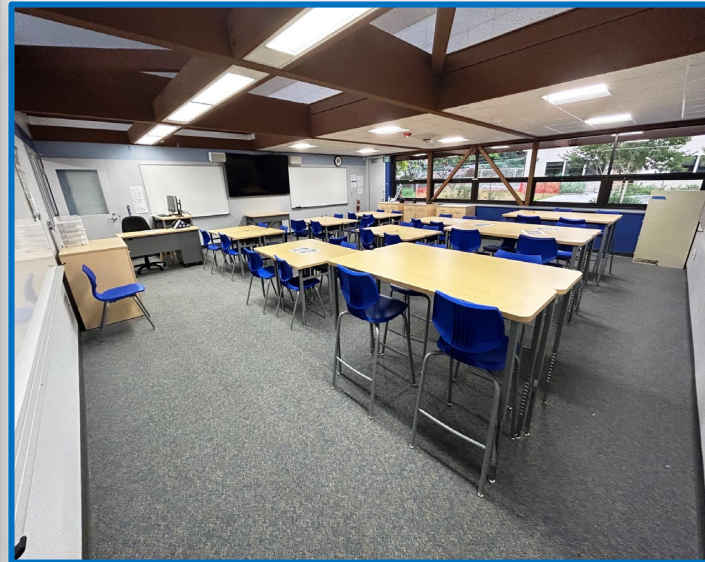

Photos as of 4/18/25



# CURRENT PROJECTS


## Diegueno Middle School – Locker Rm. Bldg. Modernization, Lunch Court Shelter & Parking Lot ADA Improvements

Start Date: 3/3/25

Estimated Substantial Completion Date: August 2025

Funding Source: Prop AA

Status: MEP rough-in, framing and concrete work

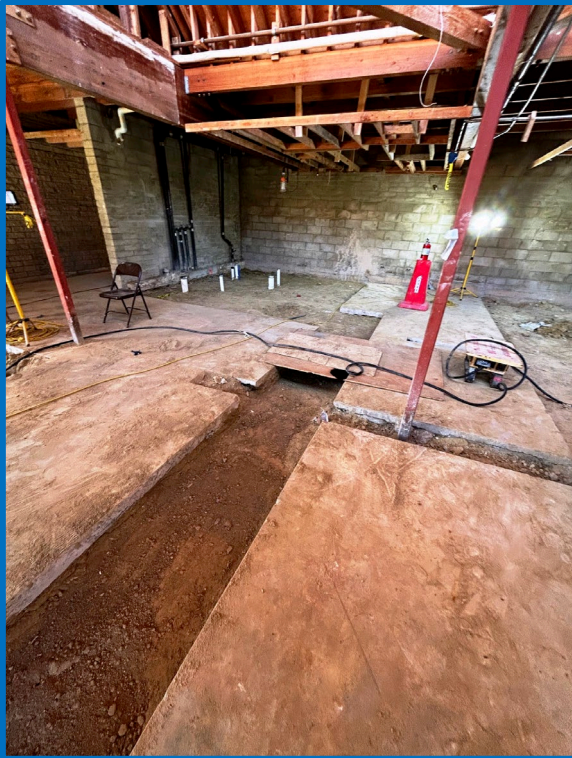

Photos as of 4/18/25





# CURRENT PROJECTS

## Oak Crest Middle School – Modernization of Crest Hall & Balance of Fire Road

Start Date: 3/3/25

Estimated Substantial Completion Date: August 2025

Funding Source: Prop AA & Mello-Roos

Status: MEP rough-in, framing, concrete work and masonry



Photos as of 4/18/25



# PROJECTS IN PLANNING

## San Dieguito High School Academy – I Bldg. Modernization Phase 2A & Balance of Mosaic Cafe

Estimated Start Date: 6/2/25

Estimated Substantial Completion Date: December 2025

Funding Source: Prop AA, Fund 35 & CFD

Status: Board awarded GMP on 3/13/25

Existing Condition of Metal Shop & Wood Shop



Photos as of 4/18/25

# PROJECTS IN PLANNING

## San Dieguito High School Academy – Locker Room Bldg. Modernization

**Estimated Start Date: Spring 2026**

**Estimated Substantial Completion Date: October 2026**

**Funding Source: Prop AA**

**Status: In construction documents phase of design**



Existing Condition



Photos as of 4/18/25

# PROJECTS IN PLANNING

## San Dieguito High School Academy – Baseball & Softball Field Modernization

Estimated Start Date: May 2026

Est. Substantial Completion Date: February 2027

Funding Source: Prop AA

Status: In design



Photos as of 4/18/25



# PROJECTS IN PLANNING

## San Dieguito High School Academy – Gym Roof & HVAC Improvements

Estimated Start Date: Winter 2027

Estimated Substantial Completion Date: Winter 2028

Funding Source: Prop AA

Status: In design



Photos as of 4/18/25

# PROJECTS IN PLANNING

## San Dieguito Sports Complex – Utilities, Communications Infrastructure & Hardcourt Improvements

**Estimated Start Date: Spring 2027**

**Estimated Substantial Completion Date: Winter 2028**

**Funding Source: Prop AA**

**Status: In design**



Photos as of 4/18/25
